

VILLE 12

Constrution Updates Report

August 2025



Project Overview

Ville 12

Masdar City, Abu Dhabi

Ville 12 is a premium residential development situated in Masdar City. The project is currently in the early stages of construction, with work progressing steadily across initial phases.





Project Narrative

Project Name: Ville 12

Type: Residential Building (2B+GF+7+R)

Plot No.: 34 (F12) Sector SE45-01 @ Masdar City

Plot Area: 4,971.34 Sq.m.


Total Built-up Area: 27,126.00 Sq.m. **Total Number of Units:** 143 Units

Contract Start Date: 15th November 2024 Q4 2024

Project Duration: 46 months

Contract Completion Date: 30th September 2028

Forecast Completion Date: 30th June 2027



Masdar City, Abu Dhabi

Progress **Overview** 20.17% 25.06%

+4.89%

Planned Progress

Actual Progress

Variance / Status (Ahead of Schedule)



Building Configuration

2 Basement Floors: Parking and Services.

Ground Floor: Residential Units, Open Landscape Area, Swimming Pools,

Amenities (Gym, Sauna, Steam Rooms), and Services.

1st to 7th Floor: Residential Units.

Roof Floor: Roof Garden.

Ongoing & Completed Activities

Enabling Works (Shoring, Piling & Excavation):


- Shoring: 374 Nos. piles casted out of 374 (100%).
- Piling: 233 Nos. central piles casted out of 233 (100%).
- Excavation: 85% Completed.
- Piles Breaking: 50% Completed.
- Capping Beams: Completed 100%.
- Piles Test: Completed 100%.
- Struts Installation: Completed 100%.
- Dewatering: Completed 100%.
- Blinding Concrete: 50% Completed.
- Tower Crane Foundation: 50% Completed.

Burtville.com

Construction Progress

Click Here

YouTube Live Stream Link

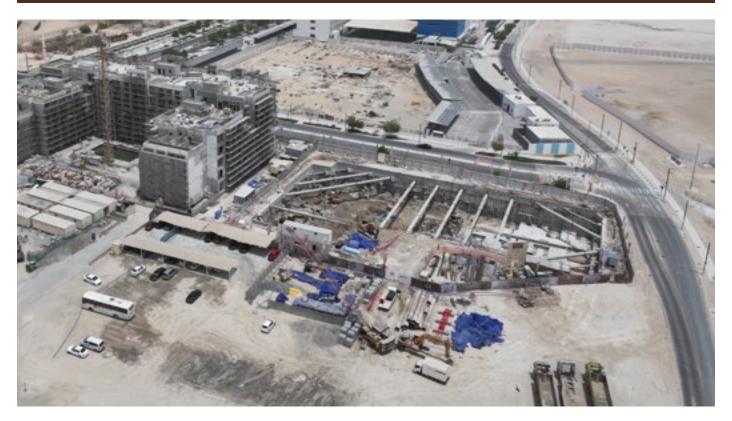





Burtville.com
